



**MHS PE Instructional Space  
Capital Project Update**

**December 6, 2016  
Study Session**

# Summary

- ▶ Project provides adequate instructional space to deliver required physical education curriculum.
- ▶ Replaces end-of-life locker room equipment.
- ▶ Provides appropriate resources for hygiene (e.g., showers, toilets, water) to meet demand of 1,500 students' daily use.
- ▶ Establishes adequate interscholastic team locker/meeting areas for boys and girls sports teams.
- ▶ Provide resources necessary to serve as the community's designated Red Cross Shelter.



## Physical Education Instructional Facilities -Increase of Three Instructional Spaces-

MHS Physical Education Instructional Space	# of Teaching Stations
Post Road Gym	2 teaching stations
Palmer Gym	2 teaching stations
Palmer Multi-Purpose Classroom	2-3 teaching stations
Free Movement Gym	1 teaching station
Restricted/Seasonal Use	
Post Auxiliary Gym/Wrestling Room 10/15 - 3/15	1 teaching station
Manchester Field (weather permitting)	1 teaching station
Track (weather permitting)	1 teaching station
Memorial Field (weather permitting)	1 teaching station

Teaching stations accommodate 30+ students or 170-200 students per period. Physical education classes are scheduled during all teaching periods.


# Mamaroneck High School

Physical Education and Locker Room Upgrades

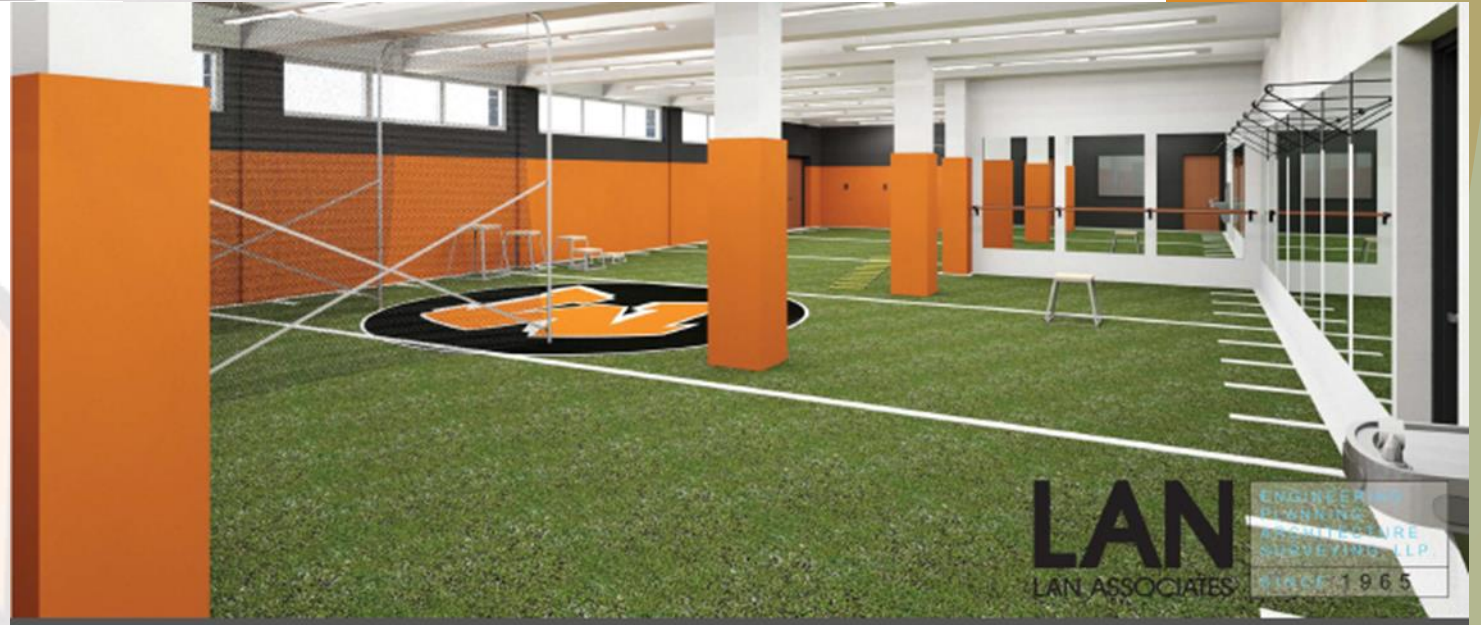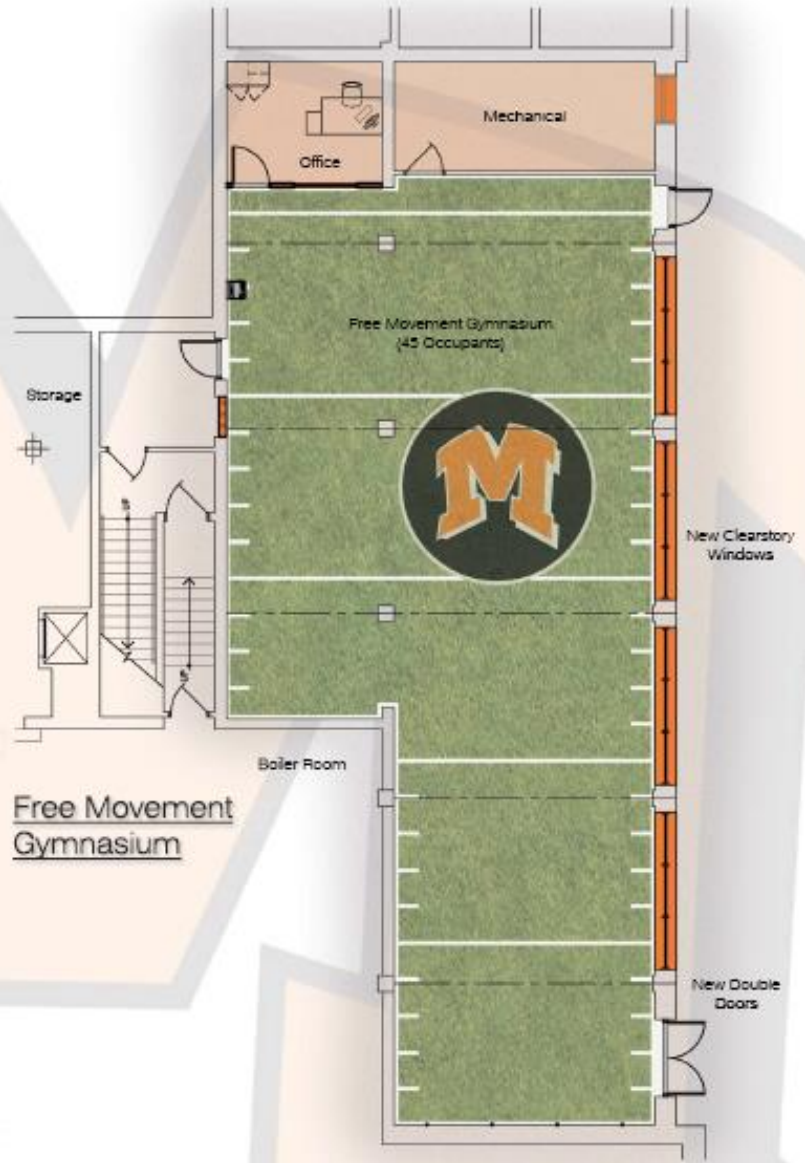

# Mamaroneck High School


Physical Education and Locker Room Upgrades

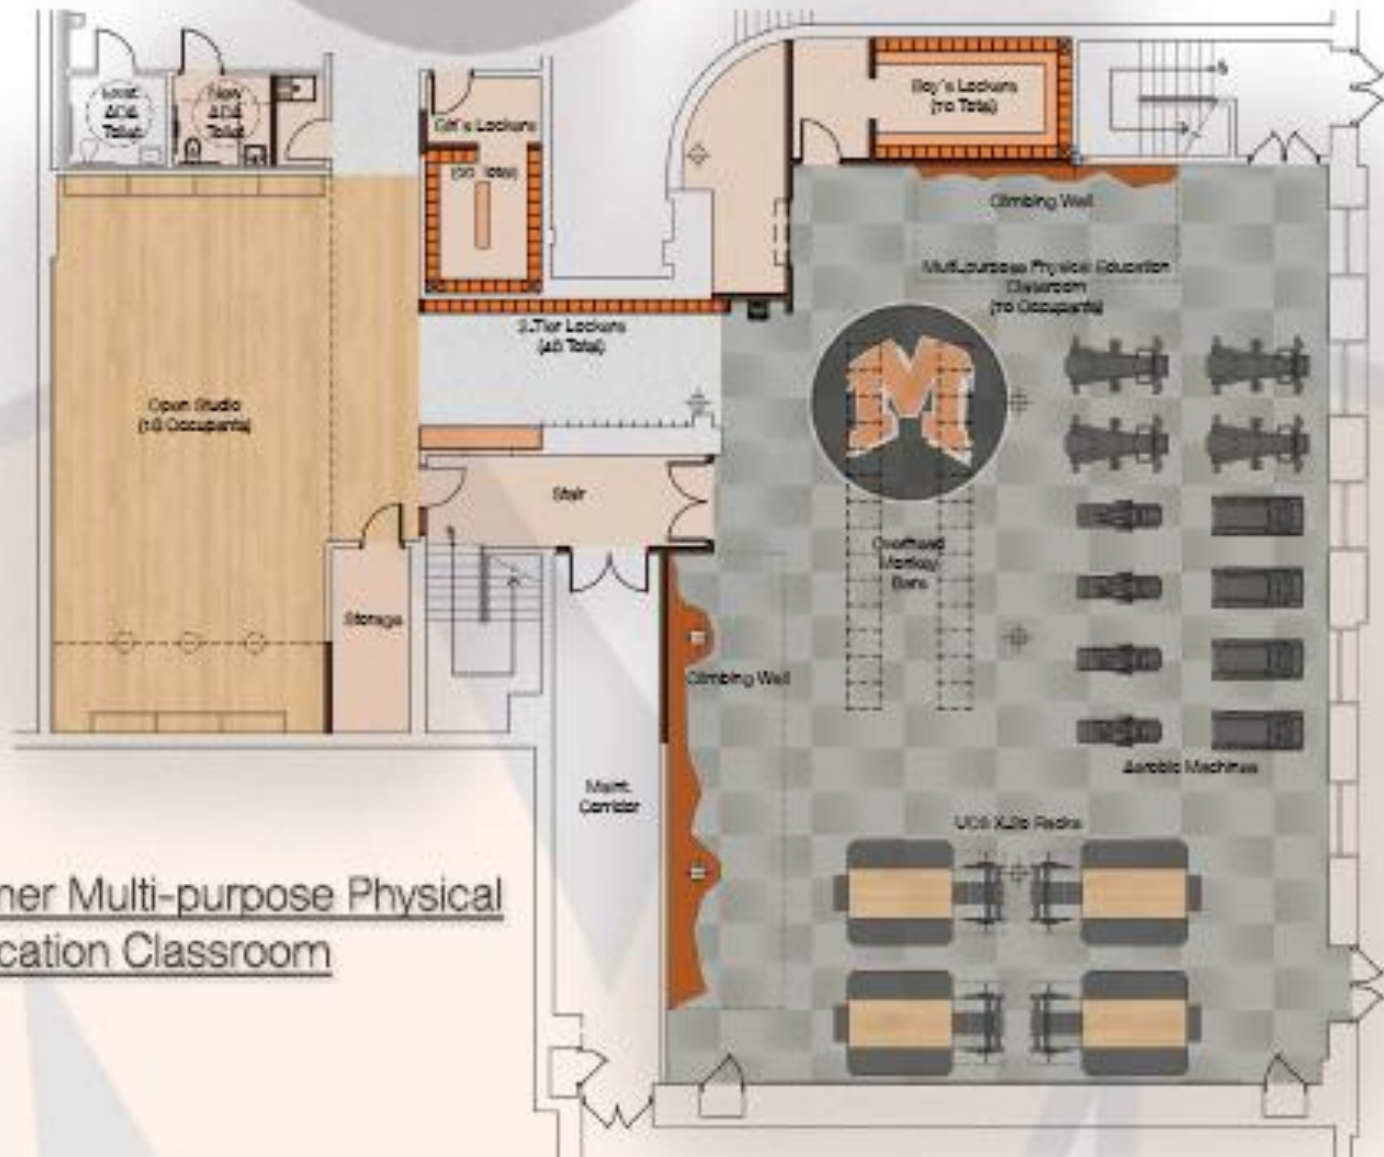

Palmer Multi-purpose Physical Education Classroom

# Mamaroneck High School

Physical Education and Locker Room Upgrades

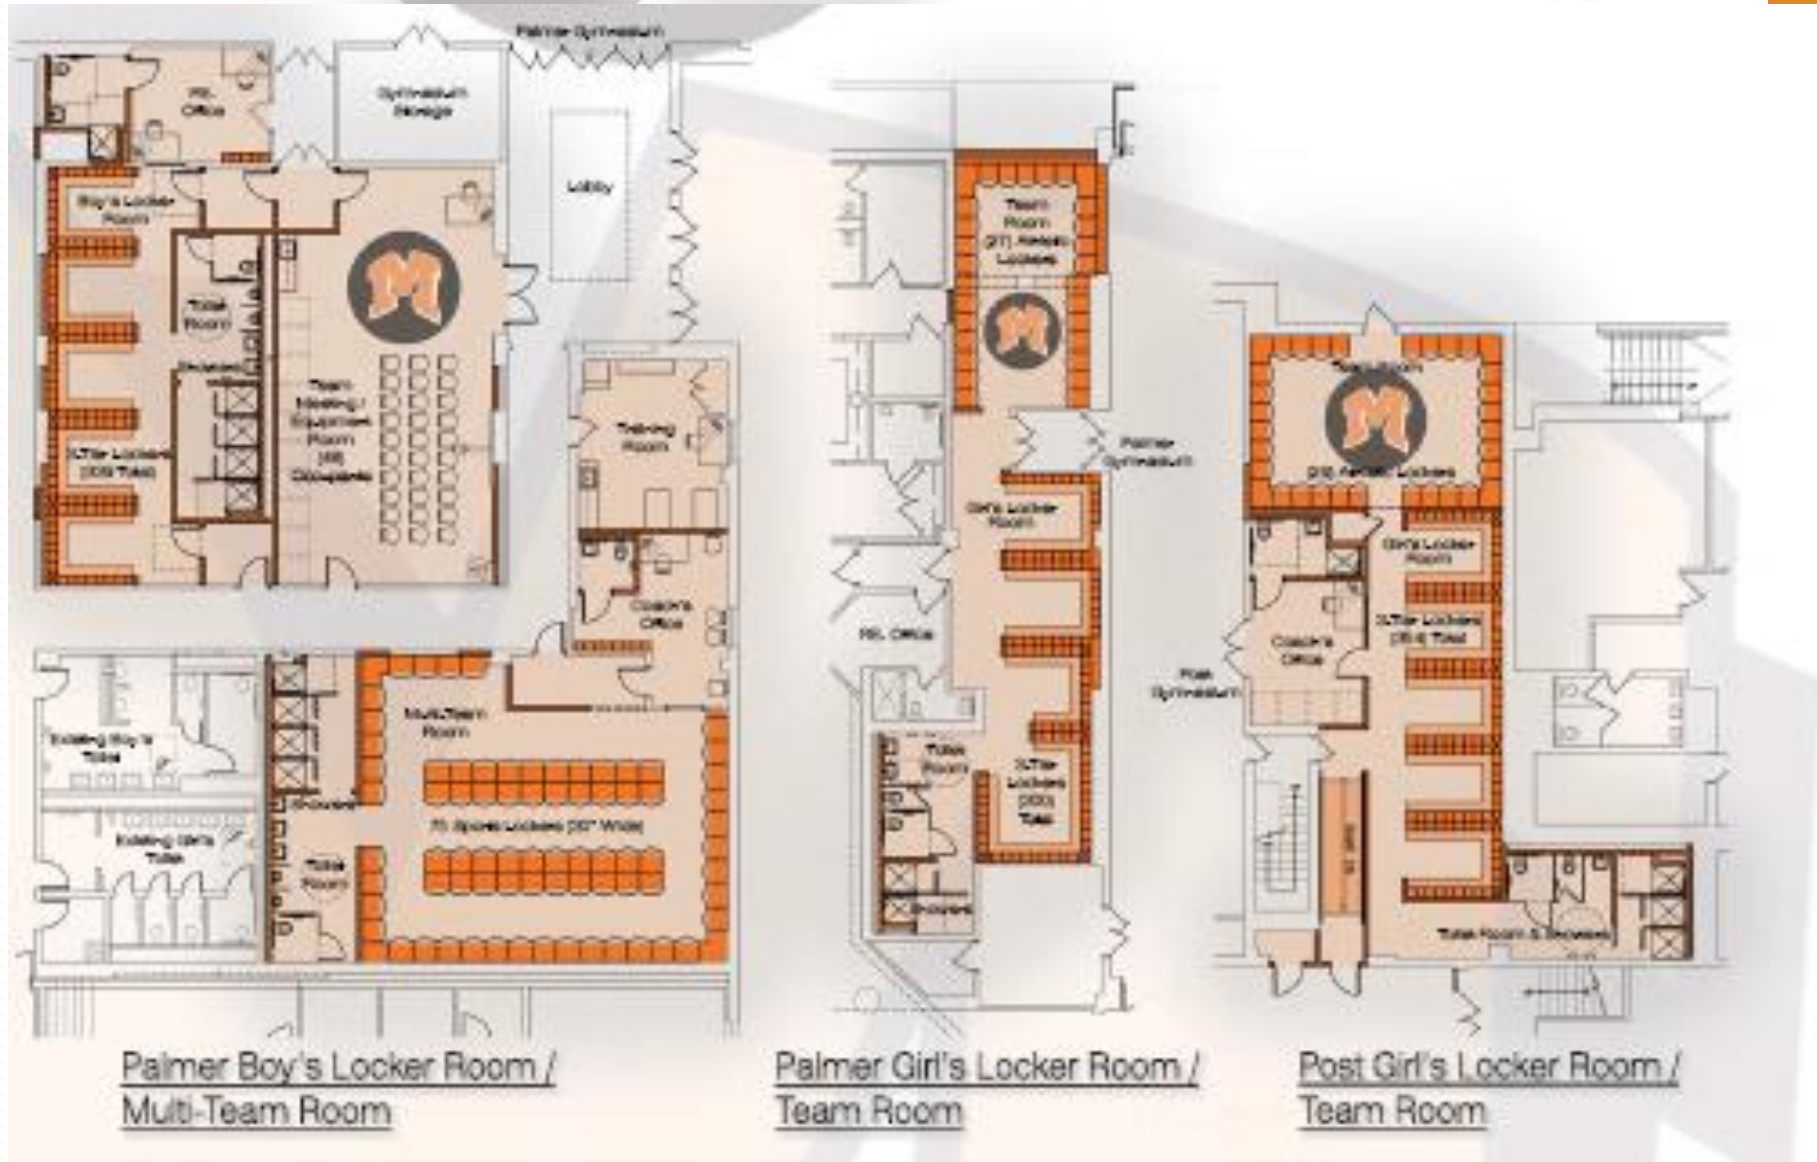

# Mamaroneck High School

Physical Education and Locker Room Upgrades



# Mamaroneck High School

Physical Education and Locker Room Upgrades





# Proposed Bond Schedule

Task	Duration	Date	Revised Dates
Bond Vote	1 day	1/12/16	1/12/16
Design	4 months	5/3/16	5/3/16
Asbestos (separated from project) SED approval		-	9/16/16
Asbestos re-bid		-	12/22/16
Asbestos award		-	1/10/17
Asbestos work		-	February & Spring Breaks
<b>Construction Work</b>			
NYSED Review*	44 weeks	3/7/17	12/26/16
Bid Preparation	2 weeks	3/21/17	1/16/17
Bidding Period	1 month	4/18/17	2/16/17
Bid Date	1 day	4/18/17	2/16/17
Award	2 weeks	5/2/17	2/28 or 3/7
Mobilization/Construction	5 months	5/3-10/2/17	4/17-10/2/17

# Curricular Priorities

- ▶ Teaching towards lifelong fitness
- ▶ Movement space for each student in the class participating
- ▶ Open space for stations
- ▶ Ability to use same space for multiple curriculum options
- ▶ Choice of activities for students-elective program for upper classmen
- ▶ Space for small sided games to maximize student participation
- ▶ Curriculum designed towards competency of skills
- ▶ Muscular strength, flexibility and cardiovascular endurance achieved through time on task and individual challenges
- ▶ Promoting personal and social responsibility where the teacher is the facilitator to learning through cues and feedback
- ▶ Reaching the goal of a physically educated physical literate individual
